


# Main Street Project Progress Update

## What's Been Going On?

Crews installed storm lines between the bridge and Kennedy, water line cut-ins near Copper Hill Square, and laid conduit—lots of conduit. Glue. Pipe. Repeat. Glue. Pipe. Repeat...Keeping track of where all those pipes go can be tricky but it will be done.

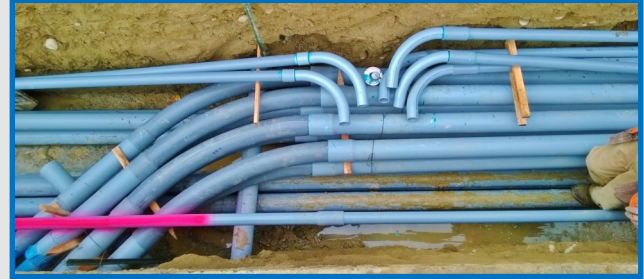

## What's Coming Up?

For the week of 10/10 the contractor will begin storm work between the bridge and Valley Street on Monday. Installing some very large 36" pipe. The water crew will continue working near Copper Hill, and may move to 143rd late in the week.




The Joint Utility Trench (JUT— power, phone, cable) crew will finish installation at Valley Street on Tuesday and then work toward Kennedy the rest of the week.

## Traffic

Traffic has been challenging, and we appreciate everyone being patient with the work. Please remember not to block driveways and intersections as you wait in the queue.



**ROAD CLOSURE—TUESDAY 10/11 8AM—4PM**  
**VALLEY STREET BETWEEN BROWN AVE AND MAIN ST**  
**CREWS WILL BE INSTALLING JUT**

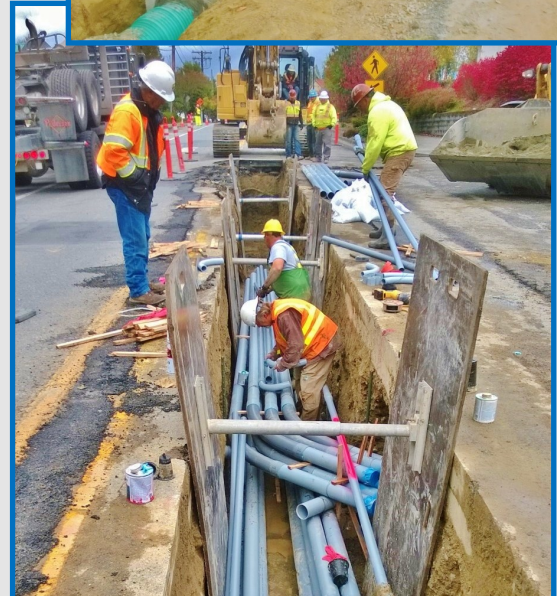

Have Questions?

Contact Shaun Tozer, Project Manager  
[shaun.tozer@duvallwa.gov](mailto:shaun.tozer@duvallwa.gov)

AND—Check us out on Facebook and Twitter.
