

Main Street Project Progress Update

What's Been Going On?

Rain, rain, go away...Poor conditions the first three days of this week resulted in very little work performed on the site. Thankfully, clear days on Thurs. & Friday allowed Interwest to complete a few of the weather-sensitive items that we've been working on. The 36" storm run is complete! Other than that it's been water line, sticking conduit together, and the cut for a retaining wall near Valley Street. Exciting stuff.



What's Coming Up next week?

For the week of 11/7 the contractor and subs will be:


- Install 18" storm between Kennedy and Coe Clemons
- Finish install of 12" water line near Kennedy, pressure test
- Install Joint Utility Trench up to Copper Hill entrance
- Fine grade and compact areas to prep for curb & gutter



For now the planned closure of Kennedy is on hold, with no estimated

Also Coming in November...

Still currently on the schedule in November is installation of light pole bases and curb gutter & sidewalk prep later in the month.

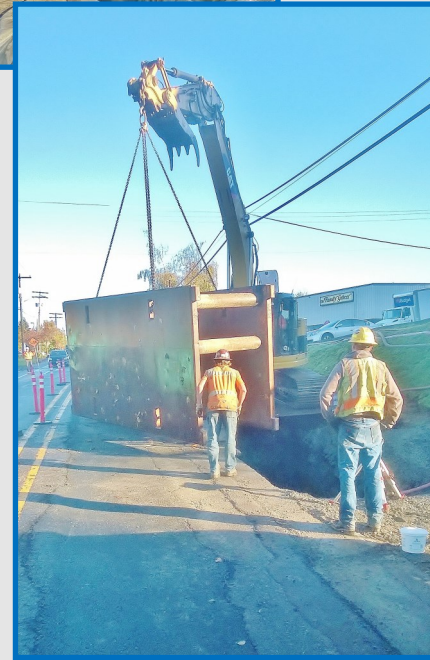

DO NOT BLOCK INTERSECTIONS AND ENTRANCES

Please make sure to stay aware of your surrounding leaving room and not blocking these areas.



Have Questions?

Contact Shaun Tozer, Project Manager

shaun.tozer@duvallwa.gov

AND—Check us out on Facebook and Twitter.
