


Main Street Project Progress Update

What's Been Going On?

It's getting a bit repetitive but this week saw quite a bit more conduit installed for the underground system, sections of water line installed and pressure tested, and some miscellaneous storm line items completed. Crews are off on Friday 11/11 in observance of Veteran's Day.

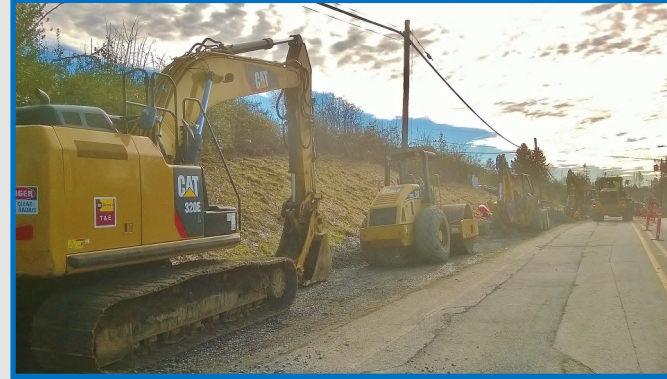

What's Coming Up next week?


For the week of 11/7 the contractor and subs will be:

- Finishing Storm line connections, setting structures
- Test and tie-in 12" water lines
- Install Joint Utility Trench to NE 145th Street
- Fine grade and compact areas to prep for curb & gutter



Help Wanted...

Don't forget, there are lots of great businesses along the project that need your support. We promise you can get there. Looks for signs like this to help guide the way.

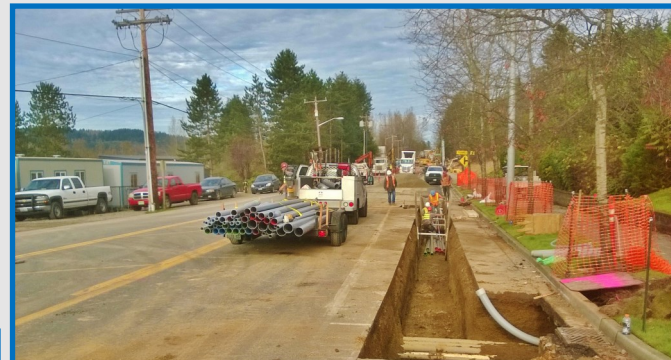

DO NOT BLOCK INTERSECTIONS AND ENTRANCES

Please make sure to stay aware of your surrounding leaving room and not blocking these areas.



Have Questions?

Contact Shaun Tozer, Project Manager

shaun.tozer@duvallwa.gov

AND—Check us out on Facebook and Twitter.
