

Main Street Project Progress Update


What's Been Going On?

Water main connections and structures was the theme of the week. Not too exciting, but productive nonetheless. We wrapped up two big connections to the water system and have placed the new pipe in-service, abandoning the old. Crews did a lot of miscellaneous work around the site too, tying up odds & ends.

What's Coming Up next week?

For the week of 11/28 the contractor and subs will be:

- Continuing storm line install around 145th and set structures
- Begin 12" water line installation from the bridge to Valley Street
- Install structures for Joint Utility Trench
- Fine grade and compact areas to prep for curb & gutter

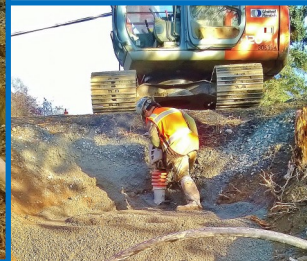

TRAFFIC REVISIONS ARE COMING

RE-STRIPING AND LANE SHIFTS BETWEEN BIG ROCK AND COPPER HILL SQUARE ARE HEADED OUR WAY—PERHAPS NEXT WEEK. WATCH FOR MORE INFORMATION ON THIS SOON.

Help Wanted...

Don't forget, there are lots of great businesses along the project that need your support. We promise you can get there. Just look for the signs and our friendly flaggers to help guide the way.

NO WORK
11/24-11/25
GOBBLE GOBBLE



Have Questions?

Contact Shaun Tozer, Project Manager
shaun.tozer@duvallwa.gov

AND—Check us out on Facebook and Twitter.
