

Main Street Project Progress Update


What's Been Going On?

This week saw a some more structures installed, storm line at 145th, and the completion of water line connections. We even snuck in some paving before old man winter struck.

What's Coming Up next week?

For the week of 12/5 the contractor and subs will be:

- Complete storm line install around 145th
- Begin JUT installation from NE 145th to NE 143rd
- Fine grade and compact areas to prep for curb & gutter
- Remove temporary patching, prep and pave with permanent repair—WEATHER DEPENDENT

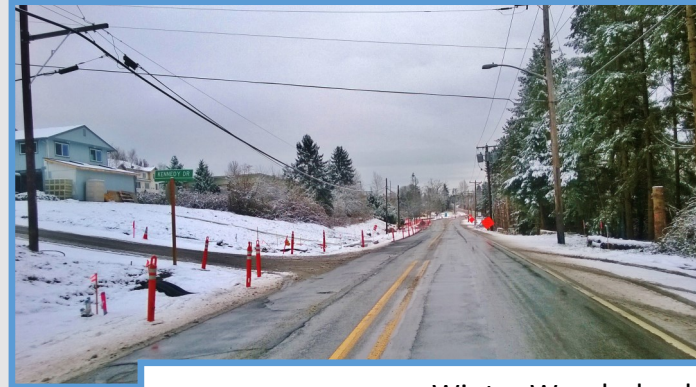


Winter Wonderland



Moving a Telephone Pole out of the way



Paving Crews in Full Swing

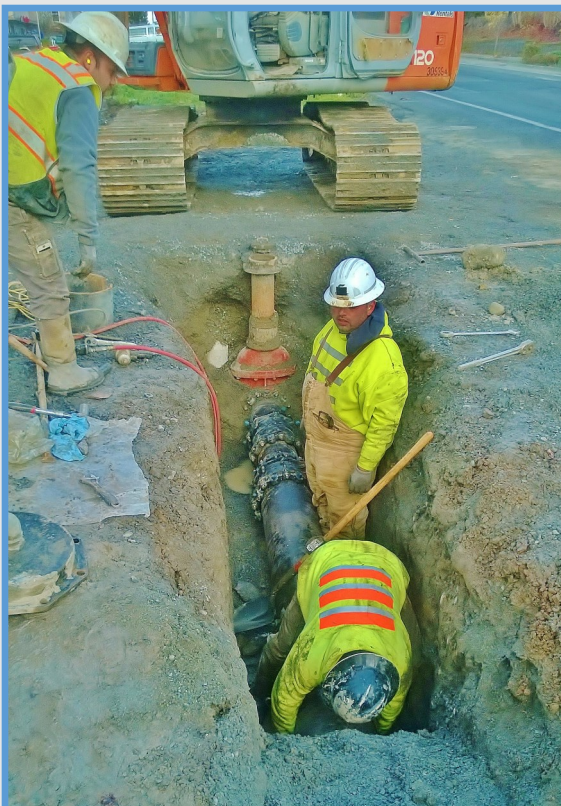

Water Main Connection at Valley Street

Help Wanted...

Don't forget, there are lots of great businesses along the project that need your support. We promise you can get there. Just look for the signs and our friendly flaggers to help guide the way.



Have Questions?

Contact Shaun Tozer, Project Manager

shaun.tozer@duvallwa.gov

AND—Check us out on Facebook and Twitter.
